



Jefferson High School

8/1/11



On August 1, the high school student parking lot was paved.

Project Update



Jefferson High School

8/3/11

Crews continue to work on the swimming pool that is scheduled to be filled on August 12.



Project Update



Jefferson High School

8/3/11



The *"Home of the Eagles"* (new gym) is taking shape. The bleachers are installed and work continues on the floor.



Project Update



Jefferson High School

8/3/11

The flooring crew installs the terrazzo flooring for the new gathering area of the high school.



Project Update



Jefferson High School

8/3/11

The new high school kitchen is a “work in progress” and will be finished in time to serve student lunches on 9/1/11.




Project Update



Jefferson High School

8/24/11

Crews put the finishing touches on the terrazzo flooring in the new gathering/cafeteria area.

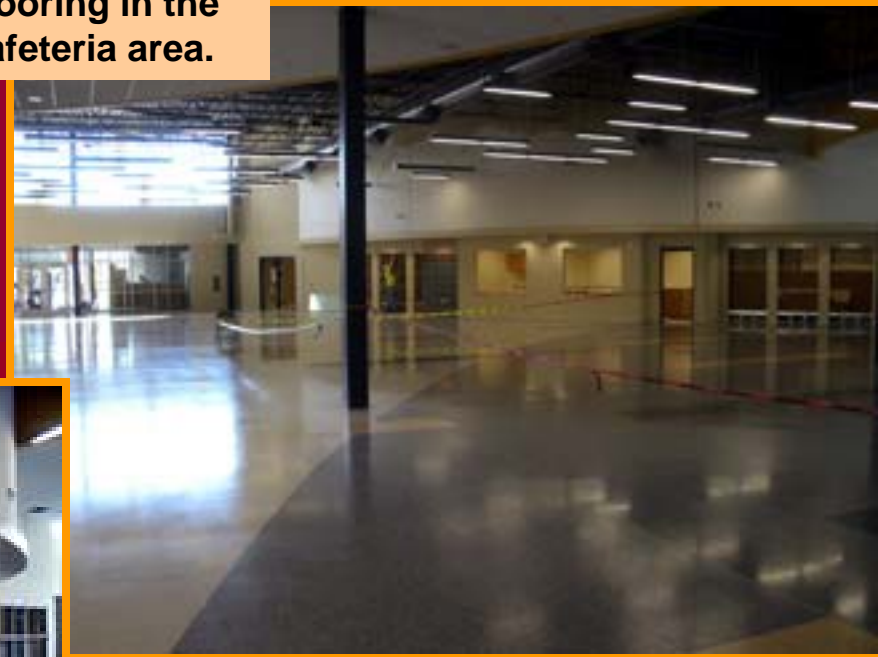

New Event Concession Stand



Project Update



Jefferson High School

8/24/11



Finishing touches are being put on the new gym, locker rooms, and shower rooms.



Project Update



Jefferson High School

8/24/11

Pictured below is the new entry for students who ride the bus to school.



The landscaping crew is on site working to finish up their portion of the project before students arrive.

Project Update



Jefferson High School

8/24/11

Food service staff, Terry Snyder and Angel Messier, are proud of their new kitchen!




New serving line at JHS.

Project Update



Jefferson High School

8/24/11

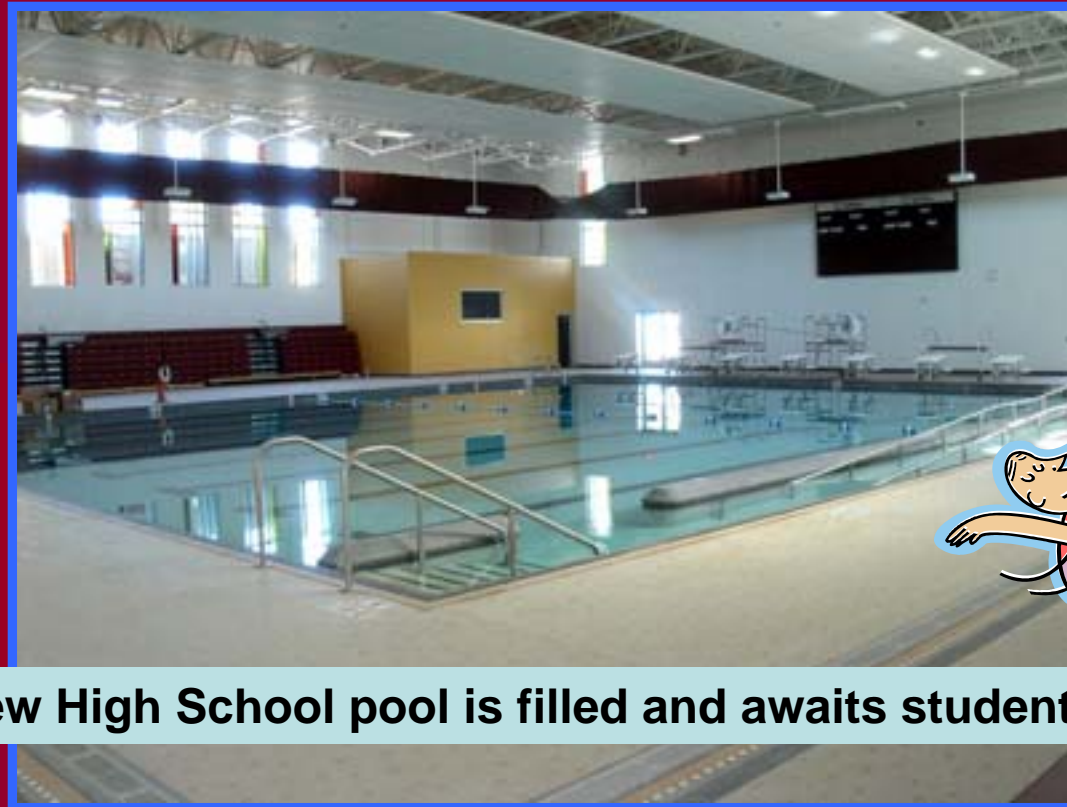

New High School pool is filled and awaits students.


Project Update



Jefferson High School

8/30/11

The new high school gathering/cafeteria area welcomed staff on August 30 and students on September 1.

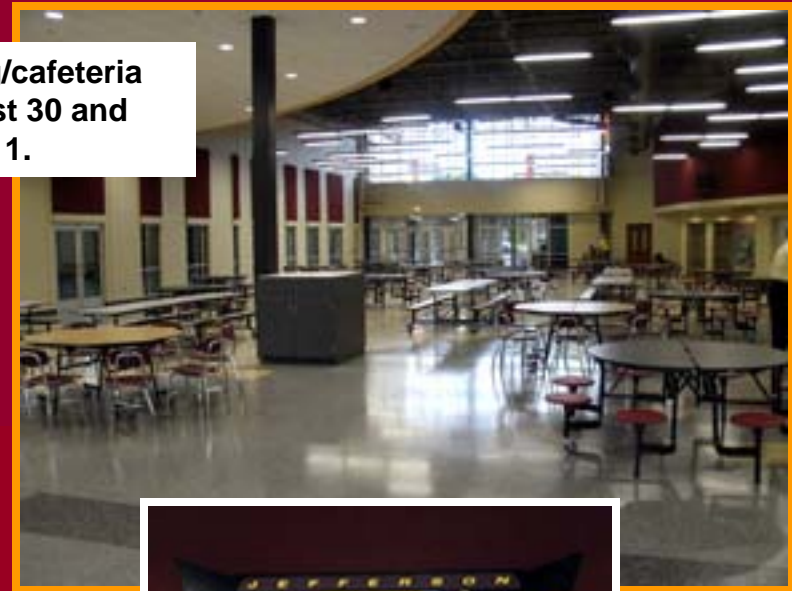

The graduating Class of 2011 donated the Eagles sign for the new gathering area.

Project Update



Jefferson High School

10/24/11

Phase II of High School Construction Project is Underway!



The various construction projects that are included in Phase II are:

- ✓ Transformation of the old small gym to the new library with location near academic wing
- ✓ Transformation of the old swimming pool to the new small gym with location near other athletic venues

The deadline for completion of Phase II projects is the end of December 2011.

Project Update



Jefferson High School

10/24/11

New library facing
the circular front
desk



Windows are
cut in from the
hallway into
the library



Soon to be study rooms inside
new library

Project Update



Jefferson High School

10/24/11



Crews work on transformation of old pool to the new gym. The deep end of the pool has been filled in and a concrete floor poured.



View of old swimming pool spectator section where a new block wall will be erected by masons.



A doorway has been cut in for the new locker rooms off of the new gym.


Project Update



Jefferson High School

12/20/11

Technology staff completes installation of computer equipment in two new computer labs off of the new library.



Project Update



Jefferson High School

12/20/11



Furniture for the new library arrives and is ready to be assembled.



Project Update



Jefferson High School

12/23/11

During winter break the finishing touches were put on the new library in preparation for the return of staff and students on January 3.




Project Update



Jefferson High School

1/6/12

2012 KICKS OFF
PHASE III OF
BUILDING
PROJECT



Project Update



Jefferson High School

1/6/12

With the asbestos abatement completed on the north side of the high school, demolition was able to begin. Once this area is removed, construction will begin on the new front entry, administration offices, and circular driveway.



Project Update
