



Jefferson High School

1/26/11

The bar joists for the swimming pool have been set and the Spancrete panels for the roof are being placed.



The masons have begun laying the block for the swimming pool locker rooms.



Project Update



Jefferson High School

1/26/11

Some excavating on the geothermal well field (football practice field) has begun. At right, crews drill a test well as they work through the process of identifying the locations for all the permanent wells.



Project Update



Jefferson High School

2/1/11

The precast panel walls for the new high school cafeteria began arriving on January 31. The crews wasted little time in swinging them into place.



Project Update



Jefferson High School

2/15/11



Currently there are four drilling rigs set up in the geothermal well field (football practice field). On average, each rig can drill one well per day. A total of 220 wells will be dug at an approximate depth of 306 feet. As of 2/11/11, 20 wells have been dug.

Project Update



Jefferson High School

2/15/11

Progress continues to be made on the new pool and gymnasium.



Southeast view of the new gymnasium.



Northeast view of the new pool, locker rooms, and gymnasium.

Project Update



Jefferson High School



Gymnasium Exterior



Gymnasium Interior

3/19/11

Project Update



Jefferson High School

3/19/11

Construction crews continue their work on the new cafeteria / gathering space for the high school.



Project Update



Jefferson High School

3/19/11



Excavation on the pool has begun. Concrete will be poured (shallow end) during the week of March 28.

Project Update



Jefferson High School

3/25/11



Project Update



Jefferson High School

4/15/11



Classrooms in the new academic wing take shape.

Project Update



Jefferson High School

4/15/11

Wires, wires, and
more wires!



Project Update



Jefferson High School

4/15/11

Pictured is the gathering area between the new pool and gymnasium on the east side of the building.



Project Update



Jefferson High School

4/15/11

Below is the entry to the gathering area with a doorway to the new swimming pool.



Above is the inside of the new gymnasium.

Project Update



Jefferson High School

4/15/11

Contractors continue their work of forming the walls/floors for the new eight lane swimming pool.



Project Update



Jefferson High School

5/4/11

Contractors begin the work of installing the windows in the new academic wing.



Project Update



Jefferson High School

5/11/11

The semi-tractor trailer carrying the vault for the geothermal system arrives on site.



Heavy equipment operators prepare the site for the placing of the vault.

Project Update



Jefferson High School

5/11/11

Equipment operators begin digging the trenches where the geothermal lines will be placed and ultimately hooked up to the vault.



Project Update



Jefferson High School

6/16/11

Curb and gutter has been poured in the new parking lot on the west side of the academic wing. Blacktop will be placed sometime over the summer.



Crews have been working on installing vinyl composition tile in the new classrooms and have also begun installing lockers.

Project Update



Jefferson High School

6/16/11



The new concession stand is moving right along. Contractors are working on the rough-ins for electrical and plumbing and will begin to put up the interior walls during the week of June 20.

Project Update



Jefferson High School

6/16/11

Masons are finishing up the brickwork for the event entry by the new gym on the southeast corner of the high school.



Project Update



Jefferson High School

6/16/11

Removal of the student parking lot has begun to make way for the construction of the new parking lot.



Project Update



Jefferson High School

6/29/11

INSIDE OF NEW ACADEMIC WING IS TAKING SHAPE!


Floor tile is being laid.



Cupboards in classrooms are being installed.



Lockers are being installed.

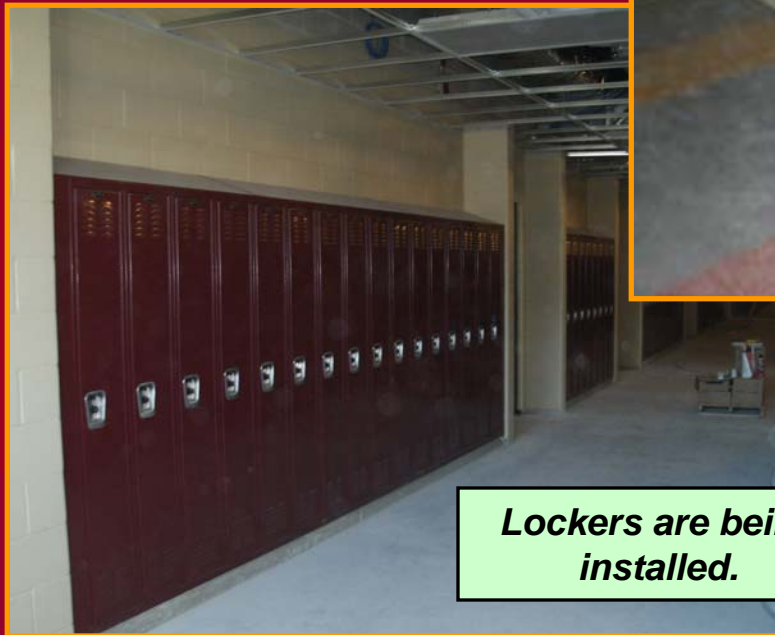

Project Update



Jefferson High School

6/29/11

Work on plumbing
in academic wing
continues.

*Toilets installed in the
girls' restroom in
academic wing.*



*Drinking fountains
installed and tile
work completed.*



Project Update




Jefferson High School

6/29/11

It won't be long now until the sound of buzzers and cheers will be heard for the JHS Eagles!

Crews prepare to lay subflooring in preparation for installation of wood floor in the new gym.




New scoreboard has been mounted.

Project Update



Jefferson High School

6/29/11



A Birdseye View



Landscape block has been laid on the northwest side of the academic wing.



Geothermal field is groomed and ready for the arrival of sod.



Birdseye view of new teacher parking lot on the northwest side of the academic wing.

Project Update



Jefferson High School

6/29/11

Roll'n in ...



... and Roll'n out



Project Update



Jefferson High School

7/7/11

Crews continue preparation work for the paving of the student parking lot.



Masons continue brickwork on new pool.



Project Update



Jefferson High School

7/19/11

One down ...



Blacktop crews paved the staff parking lot located on the west side of the new academic wing.



And one to go!

The student parking lot will be paved on August 1.

Project Update
